ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
1						
2						
3		Back frame & drywall skirting - fourth floor	15 days	Mon 7/1/19	Fri 7/19/19	
4		Fire caulking to drywall skirting - fourth floor	5 days	Mon 7/22/19	Fri 7/26/19	3
5		Install showers	3 days	Wed 7/17/19	Fri 7/19/19	3FF
6		Install backing / blocking	4 days	Mon 7/22/19	Thu 7/25/19	5
7		Electrical rough in - fourth floor	15 days	Mon 7/22/19	Fri 8/9/19	6SS
8		Mechanical rough in - fourth floor	15 days	Mon 7/22/19	Fri 8/9/19	7SS
9		Fire caulking & insulation M & E - fourth floor	5 days	Mon 8/12/19	Fri 8/16/19	8
10		Frame ceiling & bulkheads	10 days	Mon 8/12/19	Fri 8/23/19	8
11		Drywall - fourth floor	15 days	Mon 8/26/19	Fri 9/13/19	10
12		Tape - fourth floor	20 days	Mon 9/9/19	Fri 10/4/19	11FS-5 days
13		Primer coat of paint - fourth floor	4 days	Mon 10/7/19	Thu 10/10/19	12
14		Second coat of paint - fourth floor	4 days	Fri 10/11/19	Wed 10/16/19	13
15		Prime & texture ceilings - fourth floor	4 days	Thu 10/17/19	Tue 10/22/19	14
16		Install fan coil units c/w duct to mech room - fourth floor	5 days	Wed 10/23/19	Tue 10/29/19	15
17		Install t-bar ceilings to mech room - fourth floor	5 days	Wed 10/30/19	Tue 11/5/19	16
18		Install interior suite doors / caising - fourth floor	7 days	Wed 10/23/19	Thu 10/31/19	15
19		Paint doors & caising - fourth floor	8 days	Fri 11/1/19	Tue 11/12/19	18
20		Install kitchens & bath cabinets - fourth floor	7 days	Fri 11/8/19	Mon 11/18/19	19FS-3 days
21		Install lights - fourth floor	4 days	Wed 11/13/19	Mon 11/18/19	20FS-4 days
22		Install flooring - fourth floor	7 days	Thu 11/14/19	Fri 11/22/19	20FS-3 days
23		Install base board - fourth floor	5 days	Wed 11/20/19	Tue 11/26/19	22FS-3 days
24		Finish mechancial fixtures - fourth floor	6 days	Fri 11/22/19	Fri 11/29/19	23FS-3 days
25		Finish coat of paint - fourth floor	8 days	Tue 11/26/19	Thu 12/5/19	24FS-4 days
26		Finish electrical fixtures - fourth floor	3 days	Thu 12/5/19	Mon 12/9/19	25FS-1 day
27		Install wire shelving to suites - fourth floor	2 days	Thu 12/5/19	Fri 12/6/19	26SS
28		Install washroom accessories - fourth floor	2 days	Thu 12/5/19	Fri 12/6/19	27SS
29		Install suite mirriors - fourth floor	1 day	Mon 12/9/19	Mon 12/9/19	28
30		Install suite appliances & laundry room equipment	3 days	Mon 12/9/19	Wed 12/11/19	29SS
31		Final clean suites - fourth floor	3 days	Thu 12/12/19	Mon 12/16/19	30
32						
33		Insulate - corrdor & common areas	3 days	Fri 11/1/19	Tue 11/5/19	19SS
34		Drywall - corridor & common areas	5 days	Wed 11/6/19	Tue 11/12/19	33
35		Tape - corridor & common areas	7 days	Wed 11/13/19	Thu 11/21/19	34
36		Primer & first coat - corridor & common areas	3 days	Wed 11/20/19	Fri 11/22/19	35FS-2 days
37		Install stipple ceilings - corridor & common areas	2 days	Mon 11/25/19	Tue 11/26/19	36
38		Install railings & purse shelves - corridor	5 days	Wed 11/27/19	Tue 12/3/19	37
39		Install filter access hatches - corridor	1 day?	Wed 12/4/19	Wed 12/4/19	38
40		Install flooring - corridor & common area	5 days	Thu 12/5/19	Wed 12/11/19	39
41		Finish coat of paint - corridor & common area	3 days	Thu 12/12/19	Mon 12/16/19	40
42		Install light fixtures - corridor	2 days	Tue 12/17/19	Wed 12/18/19	41
43		Final clean - corridor & common area	2 days	Thu 12/19/19	Fri 12/20/19	42
44						
45		Back frame & drywall skirting - third floor	15 days	Mon 7/22/19	Fri 8/9/19	3
46		Fire caulking to skirting - third floor	5 days	Mon 8/12/19	Fri 8/16/19	45
47		Install showers - third floor	3 days	Wed 8/7/19	Fri 8/9/19	45FF
48		Install blocking / backing - third floor	4 days	Mon 8/12/19	Thu 8/15/19	47
49		Electrical rough in - third floor	15 days	Mon 8/12/19	Fri 8/30/19	45
50		Mechanical rough in - third floor	15 days	Mon 8/12/19	Fri 8/30/19	49SS
51		Fire caulking & insulation to M & E - third floor	5 days	Mon 9/2/19	Fri 9/6/19	50
52		Frame ceilings & bulkheads - third floor	10 days	Mon 9/2/19	Fri 9/13/19	50
53		Drywall - third floor	15 days	Mon 9/16/19	Fri 10/4/19	52
54		Tape - third floor	20 days	Mon 10/7/19	Fri 11/1/19	53
55		Primer coat of paint - third floor	4 days	Thu 10/31/19	Tue 11/5/19	54FS-2 days
56		Second coat of paint - third floor	4 days	Wed 11/6/19	Mon 11/11/19	55
57		Prime & texture ceilings - third floor	4 days	Tue 11/12/19	Fri 11/15/19	56
58		Install fan coil units c/w duct to mech room - third floor	5 days	Mon 11/18/19	Fri 11/22/19	57
59		Install t-bar ceilings to mech room - third floor	5 days	Mon 11/25/19	Fri 11/29/19	58
60		Install interior suite doors & casing - third floor	7 days	Mon 11/18/19	Tue 11/26/19	57
61		Paint caising & doors - third floor	8 days	Wed 11/27/19	Fri 12/6/19	60
62		Install kitchens & bath cabinets - third floor	7 days	Wed 12/4/19	Thu 12/12/19	61FS-3 days
63		Install lights - third floor	4 days	Mon 12/9/19	Thu 12/12/19	62FS-4 days
64		Install flooring - third floor	7 days	Tue 12/10/19	Wed 12/18/19	62FS-3 days
65		Install base board - third floor	5 days	Mon 12/16/19	Fri 12/20/19	64FS-3 days
66		Finish mechanical fixtures - third floor	6 days	Fri 12/13/19	Fri 12/20/19	65FS-6 days
67		Finish coat of paint - third floor	8 days	Wed 12/18/19	Mon 1/6/20	66FS-3 days
68		Finish electrical fixtures - third floor	3 days	Mon 1/6/20	Wed 1/8/20	67FS-1 day
69		Install wire shelving to suites - third floor	3 days	Thu 1/9/20	Mon 1/13/20	68
70		Install washroom accessories - third floor	3 days	Thu 1/9/20	Mon 1/13/20	69SS
71		Install suite mirriors - third floor	1 day	Tue 1/14/20	Tue 1/14/20	70
72		Install suite appliances & laundry room equipment	3 days	Tue 1/14/20	Thu 1/16/20	71SS
73		Final clean suites - third floor	3 days	Fri 1/17/20	Tue 1/21/20	72
74						
75		Insulate - corrdor & common areas	3 days	Wed 11/27/19	Fri 11/29/19	61SS
76		Drywall - corridor & common areas	5 days	Mon 12/2/19	Fri 12/6/19	75
77		Tape - corridor & common areas	7 days	Mon 12/9/19	Tue 12/17/19	76
78		Primer & first coat - corridor & common areas	3 days	Mon 12/16/19	Wed 12/18/19	77FS-2 days
79		Install stipple ceilings - corridor & common areas	2 days	Thu 12/19/19	Fri 12/20/19	78
80		Install railings & purse shelves - corridor	5 days	Mon 12/23/19	Mon 1/6/20	79
81		Install filter access hatches - corridor	1 day?	Tue 1/7/20	Tue 1/7/20	80
82		Install flooring - corridor & common area	5 days	Wed 1/8/20	Tue 1/14/20	81
83		Finish coat of paint - corridor & common area	3 days	Wed 1/15/20	Fri 1/17/20	82
84		Install light fixtures - corridor	2 days	Mon 1/20/20	Tue 1/21/20	83
85		Final clean - corridor & common area	2 days	Wed 1/22/20	Thu 1/23/20	84
86						
87		Back frame & drywall skirting - second floor	15 days	Mon 8/12/19	Fri 8/30/19	45
88		Install fire caulking to skirting - second floor	5 days	Thu 8/29/19	Wed 9/4/19	87FS-2 days
89		Install showers - second floor	3 days	Wed 8/28/19	Fri 8/30/19	87FF
90		Install blocking / backing - second floor	4 days	Mon 9/2/19	Thu 9/5/19	89
91		Electrical rough in - second floor	15 days	Mon 9/2/19	Fri 9/20/19	90SS
92		Mechanical rough in - second floor	15 days	Mon 9/2/19	Fri 9/20/19	91SS
93		Fire caulking & insulation to M & E - Second floor	5 days	Mon 9/23/19	Fri 9/27/19	92
94		Frame ceilings & bulkheads- second floor	10 days	Mon 9/23/19	Fri 10/4/19	92
95		Drywall - second floor	15 days	Mon 10/7/19	Fri 10/25/19	94
96		Tape - second floor	20 days	Mon 10/28/19	Fri 11/22/19	95
97		Primer coat of paint - second floor	4 days	Thu 11/21/19	Tue 11/26/19	96FS-2 days
98		Second coat of paint - second floor	4 days	Wed 11/27/19	Mon 12/2/19	97
99		Prime & texture ceilings - second floor	4 days	Tue 12/3/19	Fri 12/6/19	98
100		Install fan coil units c/w duct to mech room - second floor	5 days	Mon 12/9/19	Fri 12/13/19	99
101		Install t-bar ceilings to mech room - second floor	5 days	Mon 12/16/19	Fri 12/20/19	100
102		Install interior suite doors & casings - second floor	6 days	Mon 12/9/19	Mon 12/16/19	99
103		Paint doors & caising - second floor	8 days	Tue 12/17/19	Fri 1/3/20	102
104		Install kitchens & bath cabinets - second floor	7 days	Tue 12/24/19	Thu 1/9/20	103FS-3 days
105		Install lights - second floor	4 days	Tue 1/7/20	Fri 1/10/20	104FS-3 days
106		Install flooring - second floor	7 days	Wed 1/8/20	Thu 1/16/20	105FS-3 days

Project: Completion Schedule -
Date: Fri 11/15/19

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress

ID	Task Name	Duration	Start	Finish	Predecessors
107	Install base board - second floor	5 days	Tue 1/14/20	Mon 1/20/20	106FS-3 days
108	Finish mechanical - second floor	6 days	Tue 1/21/20	Tue 1/28/20	107
109	Finish coat of paint - second floor	7 days	Fri 1/24/20	Mon 2/3/20	108FS-3 days
110	Finish electrical fixtures - second floor	3 days	Tue 2/4/20	Thu 2/6/20	109
111	Install wire shelving to suites - second floor	3 days	Fri 2/7/20	Tue 2/11/20	110
112	Install washroom accessories - second floor	3 days	Fri 2/7/20	Tue 2/11/20	111SS
113	Install suite mirriors - second floor	1 day	Wed 2/12/20	Wed 2/12/20	112
114	Install suite appliances & laundry room equipment	2 days	Wed 2/12/20	Thu 2/13/20	113SS
115	Final clean suites - second floor	3 days	Fri 2/14/20	Tue 2/18/20	114
116					
117	Insulate - corrdor & common areas	3 days	Tue 12/17/19	Thu 12/19/19	103SS
118	Drywall - corridor & common areas	5 days	Fri 12/20/19	Fri 1/3/20	117
119	Tape - corridor & common areas	7 days	Mon 1/6/20	Tue 1/14/20	118
120	Primer & first coat - corridor & common areas	3 days	Mon 1/13/20	Wed 1/15/20	119FS-2 days
121	Install stipple ceilings - corridor & common areas	2 days	Thu 1/16/20	Fri 1/17/20	120
122	Install railings & purse shelves - corridor	5 days	Mon 1/20/20	Fri 1/24/20	121
123	Install filter access hatches - corridor	1 day?	Mon 1/27/20	Mon 1/27/20	122
124	Install flooring - corridor & common area	5 days	Tue 1/28/20	Mon 2/3/20	123
125	Finish coat of paint - corridor & common area	3 days	Tue 2/4/20	Thu 2/6/20	124
126	Install light fixtures - corridor	2 days	Fri 2/7/20	Mon 2/10/20	125
127	Final clean - corridor & common area	2 days	Tue 2/11/20	Wed 2/12/20	126
128					
129	Back frame & drywall skirting - main floor suites	8 days	Mon 9/23/19	Wed 10/2/19	91
130	Install fire caulking to skirting - main floor suites	3 days	Tue 10/1/19	Thu 10/3/19	129FS-2 days
131	Install showers - main floor suites	2 days	Tue 10/1/19	Wed 10/2/19	129FF
132	Install blocking / backing - main floor suites	3 days	Thu 10/3/19	Mon 10/7/19	131
133	Electrical rough in - main floor suites	10 days	Thu 10/3/19	Wed 10/16/19	132SS
134	Mechanical rough in - main floor suites	12 days	Thu 10/3/19	Fri 10/18/19	133SS
135	Fire caulking & insulation to M & E - main floor suites	5 days	Mon 10/21/19	Fri 10/25/19	134
136	Frame ceilings & bulkheads - main floor suites	10 days	Mon 10/21/19	Fri 11/1/19	134
137	Drywall - main floor suites	10 days	Mon 11/4/19	Fri 11/15/19	136
138	Tape - main floor suites	15 days	Mon 11/18/19	Fri 12/6/19	137
139	Primer coat of paint - main floor suites	4 days	Thu 12/5/19	Tue 12/10/19	138FS-2 days
140	Second coat of paint - main floor suites	4 days	Wed 12/11/19	Mon 12/16/19	139
141	Prime & texture ceilings - main floor suites	4 days	Tue 12/17/19	Fri 12/20/19	140
142	Install fan coil units c/w duct to mech room - main floor	5 days	Mon 12/23/19	Mon 1/6/20	141
143	Install t-bar ceilings to mech room - main floor	5 days	Tue 1/7/20	Mon 1/13/20	142
144	Install interior suite doors & casing - main floor suites	5 days	Mon 12/23/19	Mon 1/6/20	141
145	Paint doors & caising - main floor suites	5 days	Tue 1/7/20	Mon 1/13/20	144
146	Install kitchens & bath cabinets - main floor suites	6 days	Thu 1/9/20	Thu 1/16/20	145FS-3 days
147	Install lights - main floor suites	3 days	Fri 1/17/20	Tue 1/21/20	146
148	Install flooring - main floor suites	5 days	Wed 1/22/20	Tue 1/28/20	147
149	Install base board - main floor suites	4 days	Mon 1/27/20	Thu 1/30/20	148FS-2 days
150	Finish mechanical fixtures - main floor suites	3 days	Fri 1/31/20	Tue 2/4/20	149
151	Finish coat of paint - main floor suites	5 days	Fri 1/31/20	Thu 2/6/20	150FS-3 days
152	Finish electrical fixtures - main floor suites	3 days	Fri 2/7/20	Tue 2/11/20	151
153	Install wire shelving to suites - main floor suites	3 days	Wed 2/12/20	Fri 2/14/20	152
154	Install washroom accessories - main floor suites	3 days	Wed 2/12/20	Fri 2/14/20	153SS
155	Install suite mirriors - main floor suites	2 days	Mon 2/17/20	Tue 2/18/20	154
156	Install suite appliances & laundry room equipment	3 days	Mon 2/17/20	Wed 2/19/20	155SS
157	Final clean suites - main floor suites	3 days	Thu 2/20/20	Mon 2/24/20	156
158					
159	Insulate - corrdor & common areas	3 days	Tue 1/7/20	Thu 1/9/20	145SS
160	Drywall - corridor & common areas	5 days	Fri 1/10/20	Thu 1/16/20	159
161	Tape - corridor & common areas	7 days	Fri 1/17/20	Mon 1/27/20	160
162	Primer & first coat - corridor & common areas	3 days	Fri 1/24/20	Tue 1/28/20	161FS-2 days
163	Install stipple ceilings - corridor & common areas	2 days	Wed 1/29/20	Thu 1/30/20	162
164	Install railings & purse shelves - corridor	5 days	Fri 1/31/20	Thu 2/6/20	163
165	Install filter access hatches - corridor	1 day?	Fri 2/7/20	Fri 2/7/20	164
166	Install flooring - corridor & common area	5 days	Mon 2/10/20	Fri 2/14/20	165
167	Finish coat of paint - corridor & common area	3 days	Mon 2/17/20	Wed 2/19/20	166
168	Install light fixtures - corridor	2 days	Thu 2/20/20	Fri 2/21/20	167
169	Final clean - corridor & common area	2 days	Mon 2/24/20	Tue 2/25/20	168
170					
171	**Complete framing - main floor common**	7 days	Mon 11/4/19	Tue 11/12/19	
172	Complete mechanical rough in - main floor common	8 days	Wed 11/13/19	Fri 11/22/19	171
173	Complete electrical rough in - main floor common	8 days	Wed 11/13/19	Fri 11/22/19	172SS
174	Frame ceilings - main floor common	15 days	Wed 11/20/19	Tue 12/10/19	173FS-3 days
175	Drywall walls & ceilings - main floor common	15 days	Wed 12/11/19	Wed 1/8/20	174
176	Tape walls & ceilings - main floor common	15 days	Thu 1/2/20	Wed 1/22/20	175FS-5 days
177	Primer & first coat of paint - main floor common	5 days	Thu 1/23/20	Wed 1/29/20	176
178	Install sprinkler drops - common area	3 days	Thu 1/30/20	Mon 2/3/20	177
179	Install lights - common area	5 days	Fri 1/31/20	Thu 2/6/20	178SS+1 day
180	Install HVAC drops - common area	5 days	Mon 2/3/20	Fri 2/7/20	179SS+1 day
181	Instal ceiling tile - common area	10 days	Mon 2/10/20	Fri 2/21/20	180
182	Install glazing to pressed steel frames - common area	3 days	Mon 2/10/20	Wed 2/12/20	181SS
183	Install millwork - common area	5 days	Tue 2/11/20	Mon 2/17/20	182SS+1 day
184	Install coiling security grill - common area	2 days	Wed 2/12/20	Thu 2/13/20	183SS+1 day
185	Install ceramic floor tile - common area	7 days	Fri 2/14/20	Mon 2/24/20	184
186	Install balance of floor finishes	5 days	Fri 2/21/20	Thu 2/27/20	185FS-2 days
187	Install resident mail boxes	2 days	Fri 2/28/20	Mon 3/2/20	186
188	Finish mechanical - common area	5 days	Fri 2/28/20	Thu 3/5/20	186
189	Finish electrical - common area	5 days	Fri 2/28/20	Thu 3/5/20	188SS
190	Finish coat of paint - common area	4 days	Fri 2/28/20	Wed 3/4/20	189SS
191					
192	CAFÉ / FIRE PLACE / LIVING WALL				
193					
194					
195	**Parkade**				
196	Paint parkade walls	4 days	Mon 7/1/19	Thu 7/4/19	
197	Mechanical above grade rough in - parkade	25 days	Fri 7/5/19	Thu 8/8/19	196
198	Electrical above grade rough in - parakde	25 days	Fri 8/9/19	Thu 9/12/19	197
199	Drywall & taping to parkade walls	10 days	Fri 9/13/19	Thu 9/26/19	198
200	Fire stop / smoke seal to parkade	5 days	Fri 9/27/19	Thu 10/3/19	199
201	Install hollow metal doors	3 days	Fri 10/4/19	Tue 10/8/19	200
202	Install light fixtures	7 days	Wed 10/9/19	Thu 10/17/19	201
203	Install mechanical equipment	15 days	Fri 10/18/19	Thu 11/7/19	202
204	Install electrical equipment	15 days	Fri 10/25/19	Thu 11/14/19	203SS+5 days
205	Boiler room mechanical	75 days	Fri 10/18/19	Fri 2/7/20	202
206	Install electrical room distribution	75 days	Fri 10/18/19	Fri 2/7/20	205SS
207	Start up and comision mechancial system c/w air balance	15 days	Mon 2/10/20	Fri 2/28/20	206
208	Fire alarm verification	10 days	Mon 2/17/20	Fri 2/28/20	207SS+5 days
209					
210					
211					
212	**CHRISTMAS 12-24-2019 to 1-1-2020**				

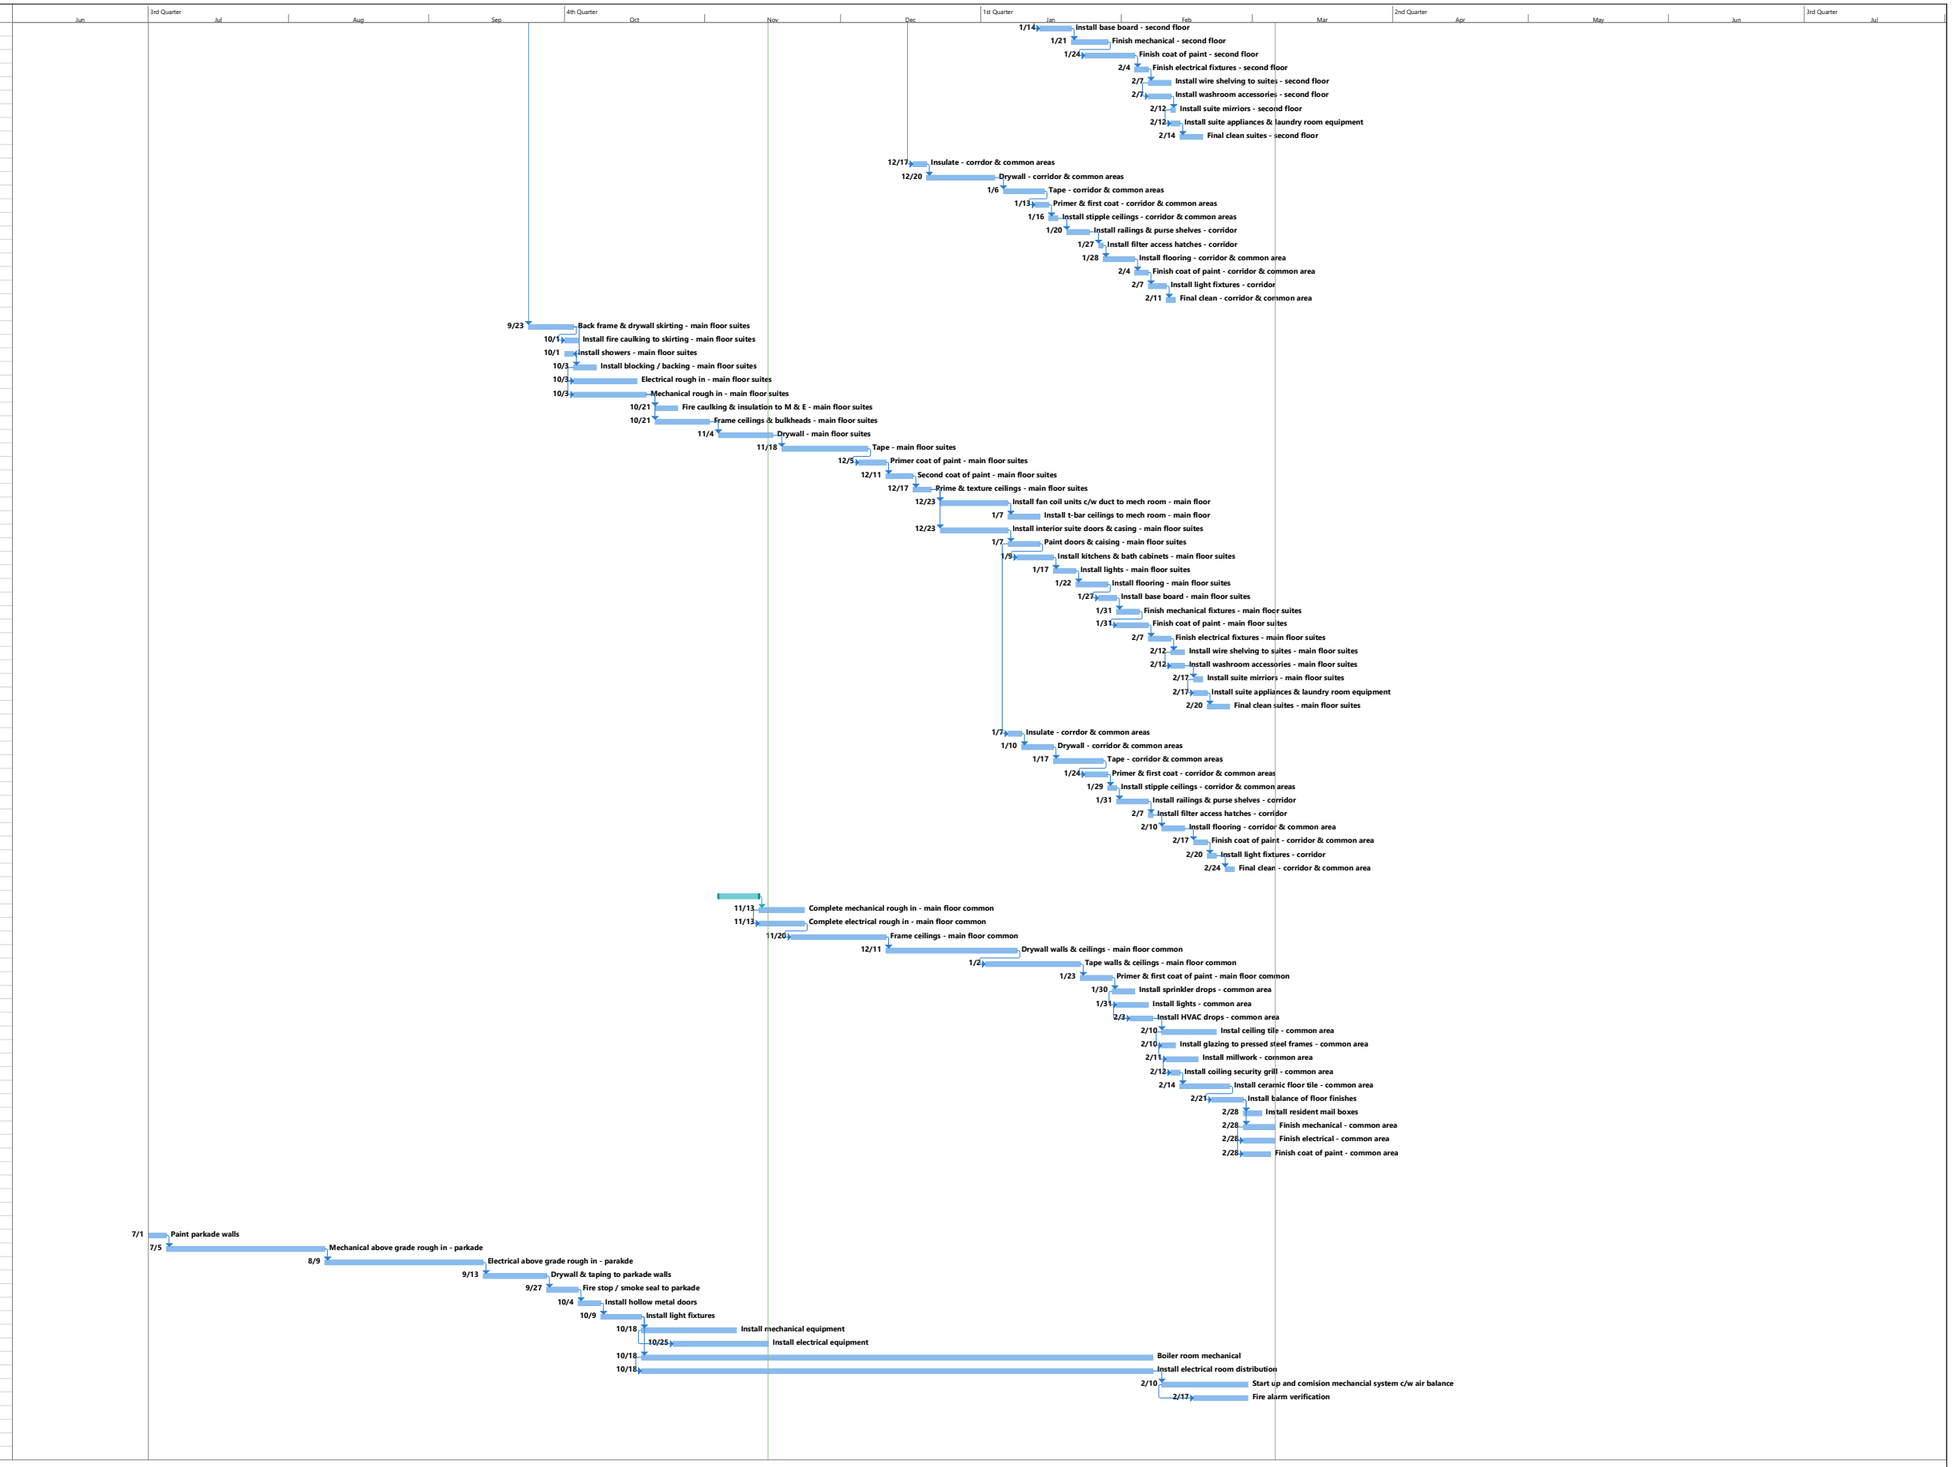

Project: Completion Schedule -
Date: Fri 11/15/19

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress
